Attachment 1 - Summary of Schedule Adjustments and Explanation (all dates are NMED complete for wells) per Integrated Schedule


Scope of work	NMED- Currently Required Date	LANL- Proposed Date	Explanation or Status
Well D MDA H (up gradient)	TBD	01/29/10	The start date of 10/01/09 sets completion as shown to allow for the required predecessor activities such as site preparation, and Task Order development and rig mobilization with the LANL subcontractor.
R-27i Water Canyon	12/15/09	12/15/09	The well is working and is ahead of the NMED required date.
CdV 37-1(i) Canyon de Valle	12/15/09	12/15/09	Working ahead of schedule. Road construction and pad preparation completed 09/21, ready for the mob of the drill rig to come off of R-27i.
Well A MDA H (down gradient)	TBD	01/29/10	Need concurrence for completion date, premobilization activities ready to start.
R-50 (Cr well)	12/31/09	02/23/10	Efficient rig scheduling pushed this to the later date. Working to better the LANL proposed date.
Well B MDA G	TBD	03/30/10	Need concurrence for completion date, premobilization activities ready to start.
MDA-AB new well	12/15/09	03/15/10	The schedule was moved out as driven by rig availability, but the later date was confirmed to support the data required for the MDA-AB investigation report (05/30/10).
R-20 (r)	TBD	03/30/10	Need concurrence for completion date, premobilization activities ready to start.
R-30 for MDA AB	12/15/09	04/29/10	Proposed date is as discussed between NMED and LANL to enable drilling rigs and crews for earlier deployment to other higher priority wells. Proposed date will meet data delivery needs.
TA-16 CME test well	not established	09/30/10	Propose date provided better rig utilization and is set for overall resource planning. The final schedule will be established at the review and approval of the aquifer pumping test plan, which is due to NMED in February 2010.
R-3	05/31/10	05/31/2010	No change
R-32 (r) TA-54	TBD	06/28/10	Need concurrence for completion date, premobilization activities ready to start.
R-22 (r) TA-54	TBD	07/30/10	Need concurrence for completion date, premobilization activities ready to start.
TW-2 (r) Pueblo Canyon	04/20/10	09/28/10	Proposed date is as discussed between NMED and LANL to enable drilling rigs and crews for earlier deployment to other higher priority wells. Proposed date will meet data delivery needs.
Buckman Sentinel	09/30/10	09/30/10	No change
Well C MDA G (down gradient)	TBD	09/28/10	Proposed date is as discussed between NMED and LANL to enable drilling rigs and crews for earlier deployment to other higher priority wells. Proposed date will meet data delivery needs.
Water Alluvials	TBD	02/12/10	Date moved forward to better use light auger rig.
Test Well P&As	01/30/10	06/21/10	Schedule was moved forward for better use of the rigs.


Illistrated Integrated Schedule Work Element Well Description May Jun Jul Aug Sep Jan Feb Mar Apr May Jun Jul Aug Sep Jan Feb Mar Jul Aug Sep Oct Nov Dec Feb Mar South Canyons NMED Complete R-27(i) Perched Water Investigation Complete CdV-37-1(i) XK MDA AB Well #2 Associated Sampling, and Data MDA AB Investigation Report F3 R-30 Associated Sampling, and Data Water Cyn Alluvials Sampling Water Canyon Investigation Report TBD Prepare Test Plan TBD Review TA-16 260 CME Aquifer Pump Test Well TBD Conduct Pump Test Prepare Report (Due June 2011)

Sandia Canyons

Archeological Site Evaluation

Cr Remediation R-50

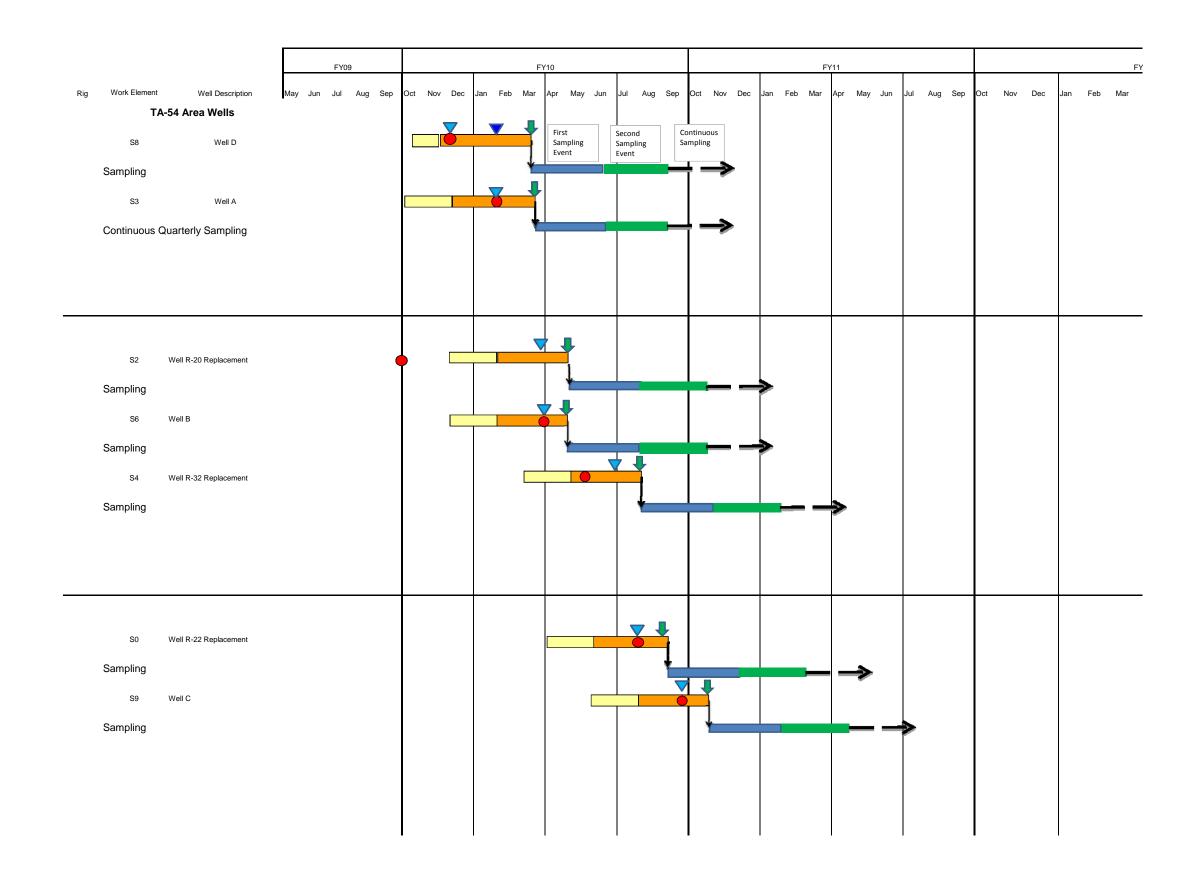

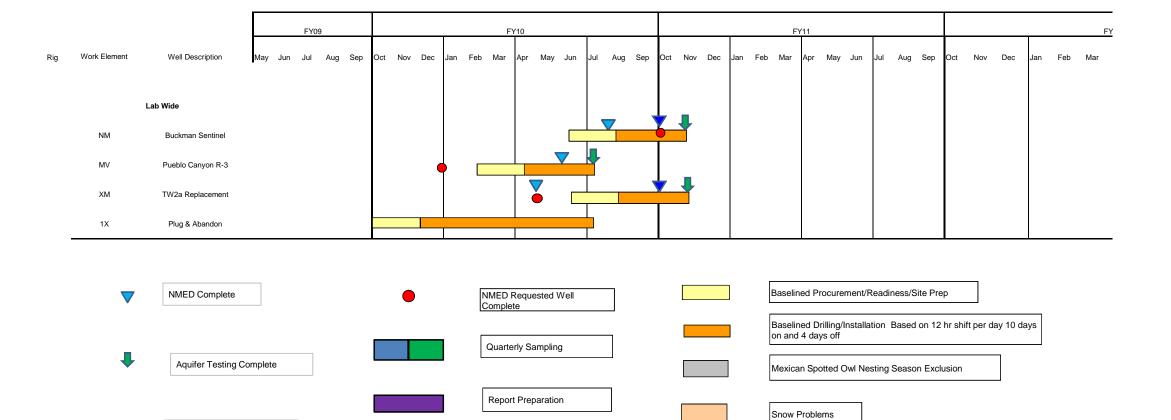

Note: updated as of 8/18/09

Adjusted NMED Complete date

